



Issued By:

Date: 19-Apr-2013

For the attention of:

Dear Sir/Madam

ARE1 TC for Asphalt Rersurfacing 2008 Nabby-Cfergus, Bel N & Lburn

Works Order Number: 36421/ARE1/1077

Please carry out the following work:

Springfield Road Phase 1 Carriageway Resurfacing

- Replace gully pots
- Cold mill 100mm
- Tack coat
- Lay 55mm binder course
- Lay 45mm surface course

Commencement Date: 29-Apr-2013 **Estimate Value:**

Works Completion Period: 10 days

Note: Contractor to acknowledge receipt of works order.

Yours Faithfully

Engineer's Representative

**WORK ORDER
CLIENT COPY**

Contact Name:
Contact number:

ARE1 TC for Asphalt Rersurfacing 2008 Nabby-Cfergus, Bel N & Lburn

Works Order Number	36421/ARE1/1077	Prepared By	
Cost Centre	Belfast North Section Office	Issue Date	19-Apr-2013
Scope	Routine	Engineer(s) Representative	
Type	Not Applicable		
Title of Works Order	Springfield Road Phase 1 Carriageway Resurfacing		

Location - **Belfast North**

HEALTH AND SAFETY	
Does CDM apply to this Works Order?	Yes
Is additional NI10 notification required?	No
Date NI10 notification sent to HSE	
CDM Coordinator	
<i>The generic Health and Safety Plan must be made Scheme Specific</i>	

WORKS ORDERS DATES	
Works Commencement Date	29-Apr-2013
Works Completion Period(days)	10
Due Date for Completion	08-May-2013
Certificate of Substantial Completion	
Due Date for Final Account	
Final Account Submitted	

COSTS	
Estimate	
How Work will be valued	Schedule of Rates

DEFECTS CORRECTION PERIOD	
Defects Correction Period(wks)	52
End of Defects Correction Period	
Works Order Completion Certificate	

Description

Replace gully pots Cold mill 100mm Tack coat Lay 55mm binder course Lay 45mm surface course

Special Requirements

--

**WORK ORDER
CONTRACTOR COPY**

Contact Name:
Contact number:

ARE1 TC for Asphalt Rersurfacing 2008 Nabby-Cfergus, Bel N & Lburn

Works Order Number	36421/ARE1/1077	Prepared By	
Cost Centre	Belfast North Section Office	Issue Date	19-Apr-2013
Scope	Routine	Engineer(s) Representative	
Type	Not Applicable		
Title of Works Order	Springfield Road Phase 1 Carriageway Resurfacing		

Location **Belfast North**

HEALTH AND SAFETY	
Does CDM apply to this Works Order?	Yes
Is additional NI10 notification required?	No
Date NI10 notification sent to HSE	
CDM Coordinator	
<i>The generic Health and Safety Plan must be made Scheme Specific</i>	

WORKS ORDERS DATES	
Works Commencement Date	29-Apr-2013
Works Completion Period(days)	10
Due Date for Completion	08-May-2013
Certificate of Substantial Completion	
Due Date for Final Account	
Final Account Submitted	

COSTS	
Estimate	
How Work will be valued	Schedule of Rates

DEFECTS CORRECTION PERIOD	
Defects Correction Period(wks)	52
End of Defects Correction Period	
Works Order Completion Certificate	

Description

Replace gully pots Cold mill 100mm Tack coat Lay 55mm binder course Lay 45mm surface course

Special Requirements

--

Project Brief

Division: Eastern Section Area: Belfast North

Brief Rev No.:

From:

To:

(RSC/Consultant)

Please design and cost the following work:

Estimated Construction Cost:

1. General Description (to be completed for all schemes)

1.1	Scheme Title:	Springfield Road (1) Carriageway Overlay
1.2	Preferred Procurement Route	<input checked="" type="checkbox"/> Term <input type="checkbox"/> One-off
1.3	Project Outcomes / Description:	To improve the existing old Asphalt Carriageway
1.4	Site(s) description (incl Route Nos. / Road Names / Towns etc)	start 12m r.h.s. springfield park to finish westcircular road
1.5	Drawings attached?	<input type="checkbox"/> No <input checked="" type="checkbox"/> Yes Details:
1.6	Utility / services information:	Service information will be supplied as per roads map and utility maps
1.7	Design standards:	
1.8	H&S / CDM Details	CDM regulations may apply Details of planning supervisor representative and H&S plan will be dependent on the contract used to execute the works. All signing/coning to be in accordance with safety at street works @ road works/chapter 8 of threew traffic signs manual.
1.9	Is this project Notifiable under CDM?	<input type="checkbox"/> No <input type="checkbox"/> Yes Details:
1.10	Symology entry:	<input type="checkbox"/> No <input checked="" type="checkbox"/> Yes Details: Client to complete
1.11	Temporary Traffic Management Requirements	
1.12	Additional info /constraints (include Costed Options, if applicable)	

2. Major / Minor Works (to be completed where Major / Minor Works form all / part of the scheme)

2.1	Background information:	Following requests from Management Inspectors on there 4 weekly Inspections,P.C.R.s This Sites scores high for this years resurfacing programme
2.2	Scope of service/deliverables:	The existing asphalt carriageway is badly crazed and breaking up due to heavy volume of traffic. The Carriageway requires planned off 100mm.tack coat, regulate were necessary.lay 55mm base and 45mm asphalt wearing course. Also all foundary type gullies are to be replaced with new c/crete pots.
2.3	Requirement for Road Safety Audit:	N/A
2.4	Environmental considerations:	No Areas identified for enviromental features
2.5	Land acquisition:	The acquisition of land is not envisaged
2.6	Accommodation works:	NO
2.7	Noise regulations:	Will apply to out of hours working if required due to close proximity of dwellings.
2.8	Legislative requirements (TO/PP etc)	Planning permission not required
2.9	Consultations/Liaisons required:	Residents to be notified of start and finished dates via a letter drop and consultation to be carried out by Road's Service Consultancy.
2.10	Responsibilities of key project persons:	
2.11	Supplementary information attached separately?	<input type="checkbox"/> No <input type="checkbox"/> Yes

3. Surface Dressing / Surface Treatment Works (to be completed where SD or ST works form all/part of the scheme)

3.1	Does project include Surface Dressing / Surface Treatments?	<input type="checkbox"/> No <input type="checkbox"/> Yes ↓
-----	---	--

3.2	Confirm that the Annual Surface Dressing / Surface Treatment schedule is attached	<input type="checkbox"/> No	<input type="checkbox"/> Yes
3.3	If additional SD / ST scheme/s to the original Schedule, forward details to the appropriate RSC Centre.	<input type="checkbox"/> No	<input type="checkbox"/> Yes (RSC to complete Project Change Control form)

[Hyperlink to Spreadsheet](#)

4. Resurfacing Works (to be completed where Resurfacing forms all/part of the scheme.)			
4.1	Does project include Resurfacing?	<input type="checkbox"/> No	<input checked="" type="checkbox"/> Yes ↓
4.2	Section & Chainage:	start 12m r.h.s. springfield park finish westcircular road	
4.3	Total length:	500m x 11m = 5,500sqm 3 lanes 1.5km	
4.4	Materials / courses:	tack coat,regulate, 55mm base and 45mm asphalt waering	
4.5	Regulating requirements:	were necessary	
4.6	Drainage requirements:	replace all foundary pots with new c/crete pots	
4.7	Road support requirements:	N/A	
4.8	Kerbing requirements:	N/A	
4.9	Entrances:	N/A	
4.10	Patching requirements	<input checked="" type="checkbox"/> No	<input type="checkbox"/> Yes Details: Client to complete
4.11	Safety barriers issues:	<input checked="" type="checkbox"/> No	<input type="checkbox"/> Yes Details:
4.12	Traffic flow figures:		
4.13	Deflectograph data:	N/A	
4.14	Traffic considerations:		
4.15	Traffic sensitive street:	<input type="checkbox"/> No	<input type="checkbox"/> Yes Details:
4.16	Combined scheme with other Client:	<input checked="" type="checkbox"/> No	<input type="checkbox"/> Yes Details:
4.17	Supplementary information attached separately?	<input type="checkbox"/> No	<input type="checkbox"/> Yes

5. Programme Information / Key Target Dates (all schemes)

5.1	Key Target date – Design Completion:	2013 - 2014		
5.2	Key Target date – Cost Estimate:	Preliminary		Final Estimate to be approved by Client prior to Works Order issue
		Final		
5.3	Key Target date – Construction Commencement:			
5.4	Monitoring meeting(s) required:	<input type="checkbox"/> No	<input type="checkbox"/> Yes	Details:
5.5	Scheme / Section Office Contact(s):			
5.6	Other relevant scheme contacts:			

6. Account NI Coding (all schemes)

Org	Cost Centre	Account Code	Analysis 1	Analysis 2	Analysis 3	Spare
141	36421	70000	000000		B50081	000000

Signed (Client): _____

Grade: _____

Date: 19/02/13

N.B: Grade of all signatories is to be in accordance with Account NI Delegation Limits and at least HPTO.

7. Consultant's Use only

Work to be carried out by (Consultant to complete & agree at PDMG):	RSC	<input type="checkbox"/>	Amey OW	<input type="checkbox"/>	Joint Team	<input type="checkbox"/>
---	-----	--------------------------	---------	--------------------------	------------	--------------------------

The brief above has been considered in accordance with the RSC QMS Procedure R-S-08: Brief Review. The brief is accepted / rejected (select appropriate box). The Client has been informed of the decision.


Signed:

Date:

Consultant's Job Number:

[Go to guidance](#) on the completion of this document.





Springfield Carriageway Overlay (12m rhs springfield park to westcircular road) (1)

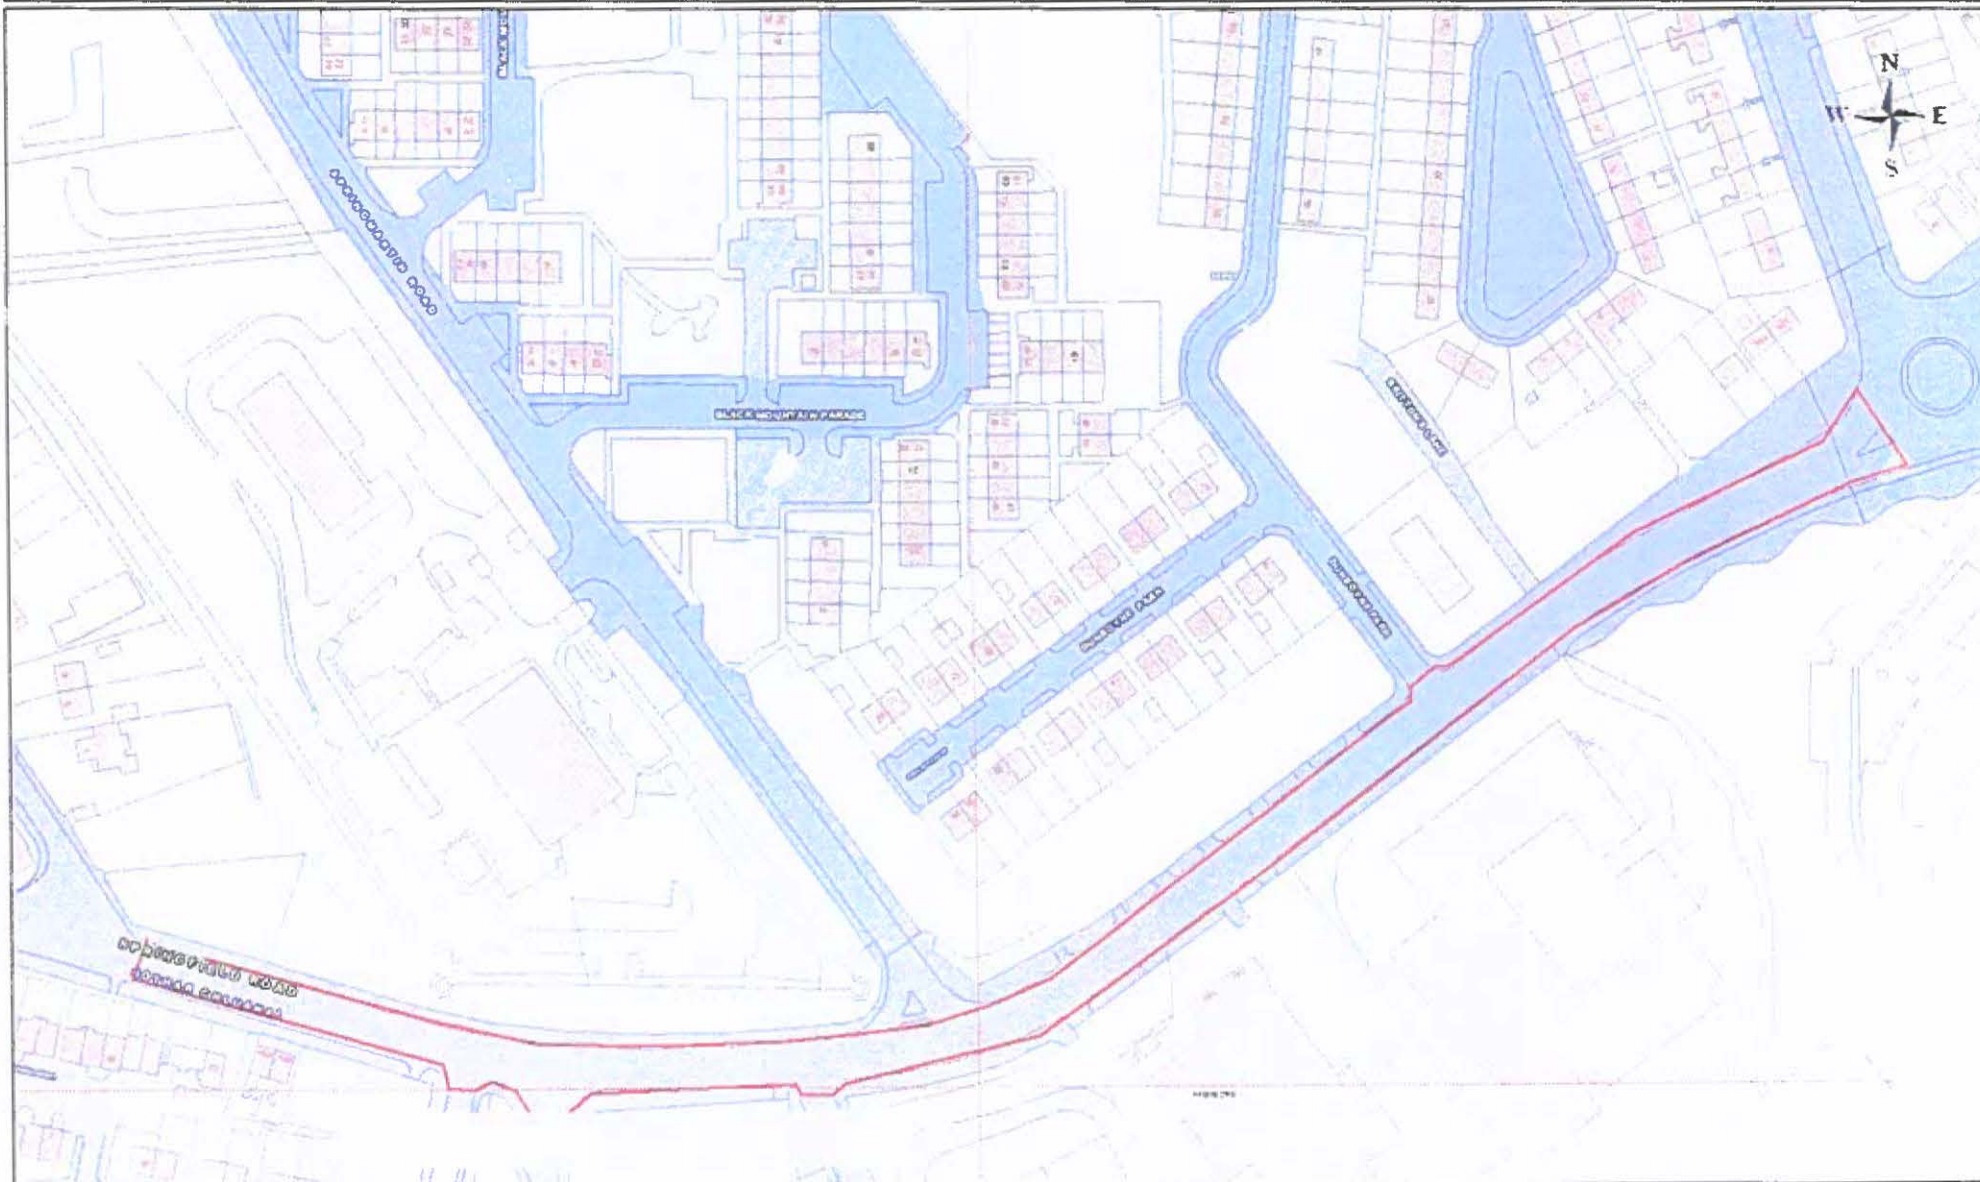

This material is based upon Crown Copyright and is reproduced with the permission of Land and Property Services under delegated authority from the Controller of Her Majesty's Stationery Office. © Crown copyright and database rights NIMA ES&LA214

Scale 1/1800
Centre = 330808 E 374125 N

Date 16/2/2011

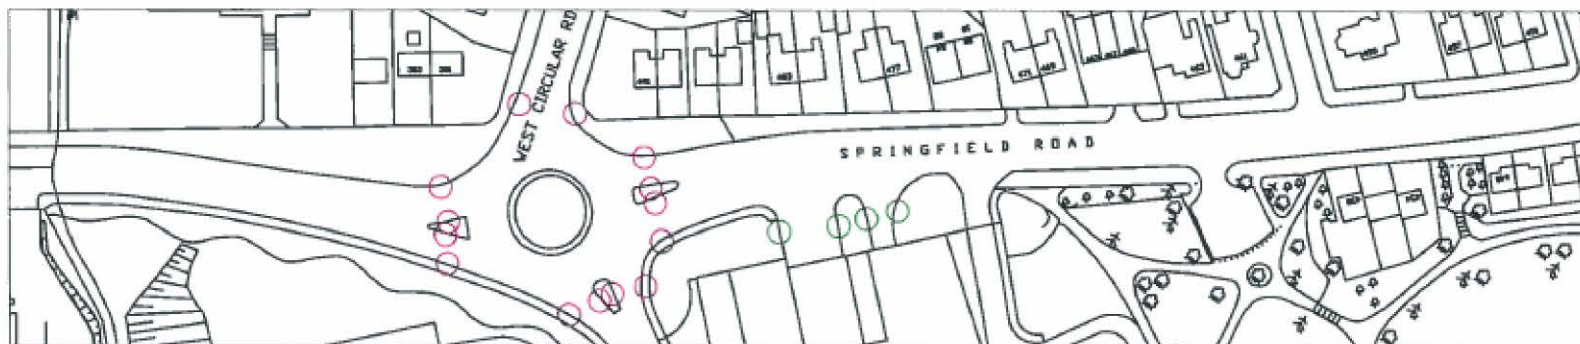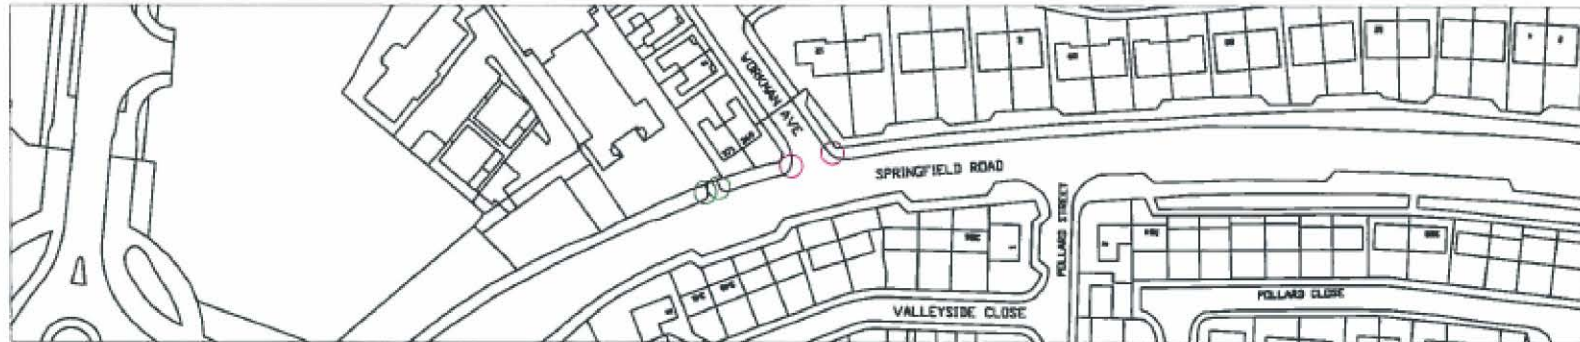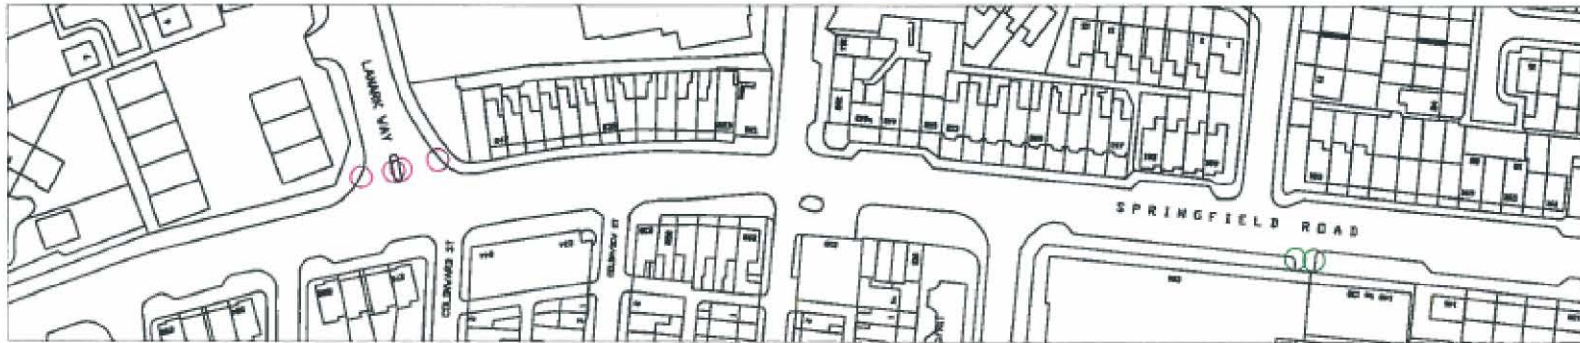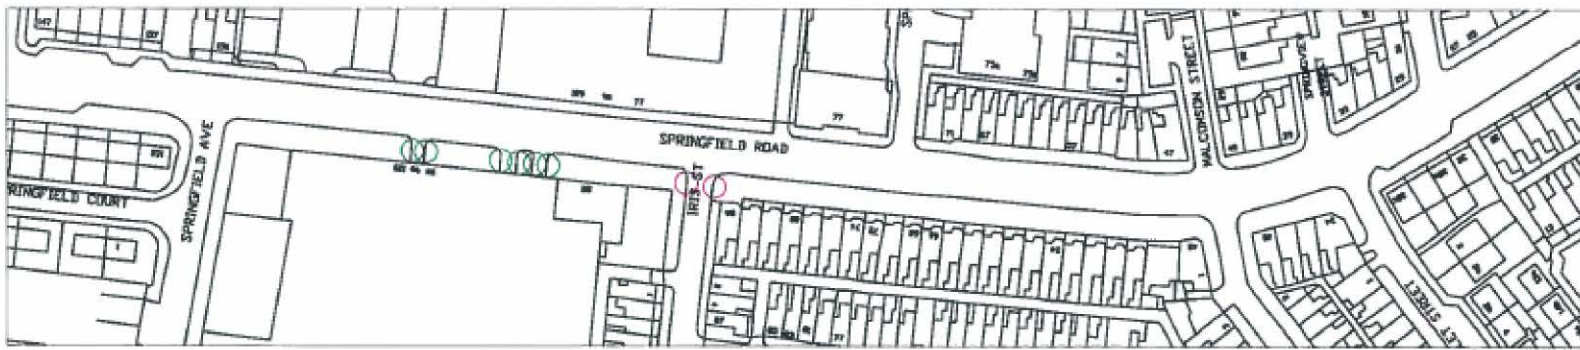

NO.	REVISION	DATE
-----	----------	------

'Based upon Ordnance Survey of Northern Ireland's data with the permission of the controller of Her Majesty's Stationary Office, © Crown copyright and database rights NIMA ES&LA214'.
 'Unauthorised reproduction infringes © Crown copyright and may lead to prosecution or civil proceedings'.

Project **SPRINGFIELD ROAD BELFAST**

Title **PROPOSED DROPPED KERBS**

FILE NO.	DESIGNED	date	2/17
DRAWN RD	CHECKED	date	
TRACED	APPROVED	date	
Dwg. No.	Revision		

Scales

transportni

EASTERN DIVISION

Hydebank
 4 Hospital Road
 Belfast BT8 8JL

Tel : 02890 253000
 Fax : 02890 253220
